LEADERSHIP BRIEFING

Bank Agentic AI Platform

Bank_Agentic_Sam — Scrum delivery plan (Jira project BAS)

Saleem | October 2026

Why we are building a governed agentic AI platform

- A controlled agent that plans multi-step work and runs banking workflows using only approved tools
- Start with high-value, low-risk use cases, backed by measurable success KPIs
- One reference architecture: identity, retrieval, tools, governance and observability
- Success: v1.0 security-tested, UAT-approved and released to the production population

KEY MESSAGE

Governed, auditable AI for authenticated bank employees, live by 29 Dec 2026.

SCOPE

Nine epics define the platform scope

01 Discovery & Architecture

BAS-1 · Use cases, MVP scope, KPIs and reference architecture

02 Identity & Access

BAS-2 · SSO, entitlements, session isolation, fail-closed access

03 Data & Integrations

BAS-3 · Governed connectors, data contracts and audit logging

04 RAG & Knowledge

BAS-4 · Entitlement-aware retrieval with source citations

05 Agent Orchestration

BAS-5 · Planner, tool registry, human approval for high-risk actions

06 AI Governance

BAS-6 · Prompt-injection defense, PII handling, approval gates

07 LLMOps & Observability

BAS-7 · Evaluation sets, versioning, traces, cost and latency

08 QA, Security & UAT

BAS-8 · Functional, red-team, performance and business UAT testing

09 Release & Adoption

BAS-9 · Phased rollout, runbooks, training, support and adoption

DELIVERY APPROACH

Scrum in Jira Cloud: team-managed project BAS, board 235

6

Sprints

Two-week sprints, 6 Oct – 28 Dec 2026

3

Releases

v0.1 Foundation, v0.5 Controlled Pilot, v1.0 Production

9

Epics

BAS-1 to BAS-9, one per capability theme

71

Work items

9 epics, 19 stories, 9 tasks, 4 bugs, 30 subtasks

Hierarchy: Epic → Story / Task / Bug → Subtask. Feature = Story + 'feature' label; AI Control = Task + 'ai-control' label.
Scrum reports: burndown, sprint report and velocity, reviewed during each sprint and at retrospectives.

RELEASE ROADMAP

Three releases to production by 29 Dec 2026

6–19 Oct 2026

v0.1 Foundation

- Approved MVP scope and architecture
- SSO identity
- User isolation foundation

20 Oct – 30 Nov 2026

v0.5 Controlled Pilot

- Governed RAG and agent orchestration
- AI guardrails and observability
- Ready for controlled pilot

1–29 Dec 2026

v1.0 Production

- Security-tested and UAT-approved
- Released to the defined production population
- Support and escalation active

SIX SPRINTS

Six two-week sprints, 6 Oct – 28 Dec 2026


S1	S2	S3	S4	S5	S6
6 – 19 Oct	20 Oct – 2 Nov	3 – 16 Nov	17 – 30 Nov	1 – 14 Dec	15 – 28 Dec
Foundation & Access Finalize MVP scope, architecture, SSO identity, user-context isolation and the first governed knowledge slice.	**RAG & Knowledge** Governed ingestion, entitlement-aware retrieval, citations and freshness controls.	**Agent Orchestration** Planning, approved tool execution, human approvals and core banking agent workflows.	**Governance & LLMOps** Harden AI guardrails, privacy, observability, evaluation, cost and model/prompt version controls.	**Security QA & UAT** Red-team testing, resilience, defect remediation and business UAT.	**Production & Adoption** Controlled rollout, training, support readiness, adoption measurement and production release.

71 Jira issues across five work types

Work type	Count	Includes	Example in Jira	Used for
Epic	9	BAS-1 – BAS-9	BAS-4 RAG & Governed Knowledge	**Business and technology themes**
Story	19	10 stories + 9 Features	BAS-14 SSO and session context	**User value, with acceptance criteria**
Task	9	8 tasks + 1 AI Control	BAS-30 PII masking and retention	**Architecture, UAT, standards, operations**
Bug	4	One each in sprints S2–S5	BAS-34 Telemetry privacy bug	**Reproduction, actual, expected, impact**
Subtask	30	Created under parent items	BAS-44 Profile API contract	**Granular implementation steps**
Total	**71**	**Plus 9 dependency links**	**BAS-41 kept for Phase 2**	

CRITICAL PATH

Nine dependency links converge on the v1.0 deploy

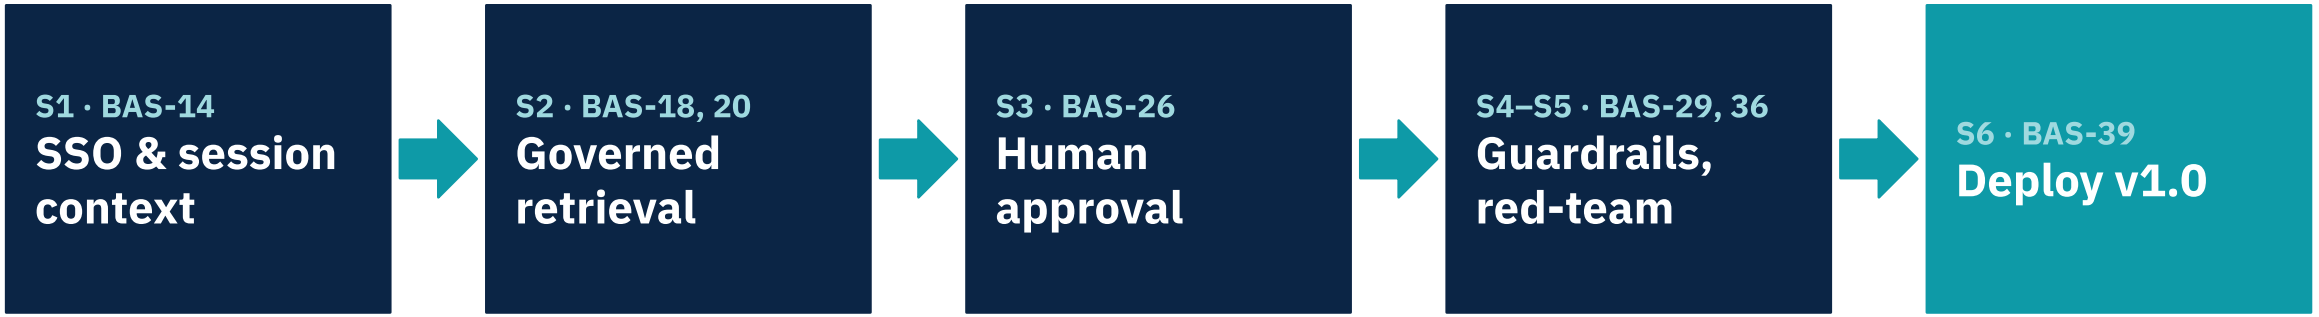

Blocks BAS-18 employee profile and entitlement API (S2)

BAS-20 also blocked by critical session-cache bug BAS-16; BAS-21 relates to planner BAS-25

Blocks the v1.0 production deploy BAS-39

Prompt-injection defenses block red-team tests; BAS-32 trace evidence relates

Blocked by BAS-26, UAT sign-off BAS-37 and privacy bug BAS-34

Watch item: BAS-39 cannot ship until human approval (BAS-26), business UAT sign-off (BAS-37) and the telemetry privacy bug (BAS-34) are closed.

GOVERNANCE

AI controls and review gates built into delivery

AI guardrails and privacy (BAS-6, BAS-7)


- **Prompt-injection defense**
  Unsafe requests denied and logged (BAS-29)
- **PII masking and retention**
  AI Control BAS-30, validated before release
- **Human-in-the-loop approval**
  High-risk actions pause for approval (BAS-26)
- **Audit and trace logging**
  End-to-end trace IDs and audit correlation (BAS-32)

Assurance and sign-off gates (BAS-8)

- **Code Review → AI & Security Review**
  Guardrails, IAM, privacy and RAG/tool safety checked
- **Red-team and security testing**
  Adversarial suite BAS-36; evidence retained
- **Business UAT sign-off**
  UAT and release-readiness review (BAS-37)
- **Ready for Release**
  No unresolved Critical/Highest defects; approval recorded

Planned workflow gates (workbook 04_WORKFLOW) — not yet configured in Jira BAS

Recommended structure: team and reporting lines

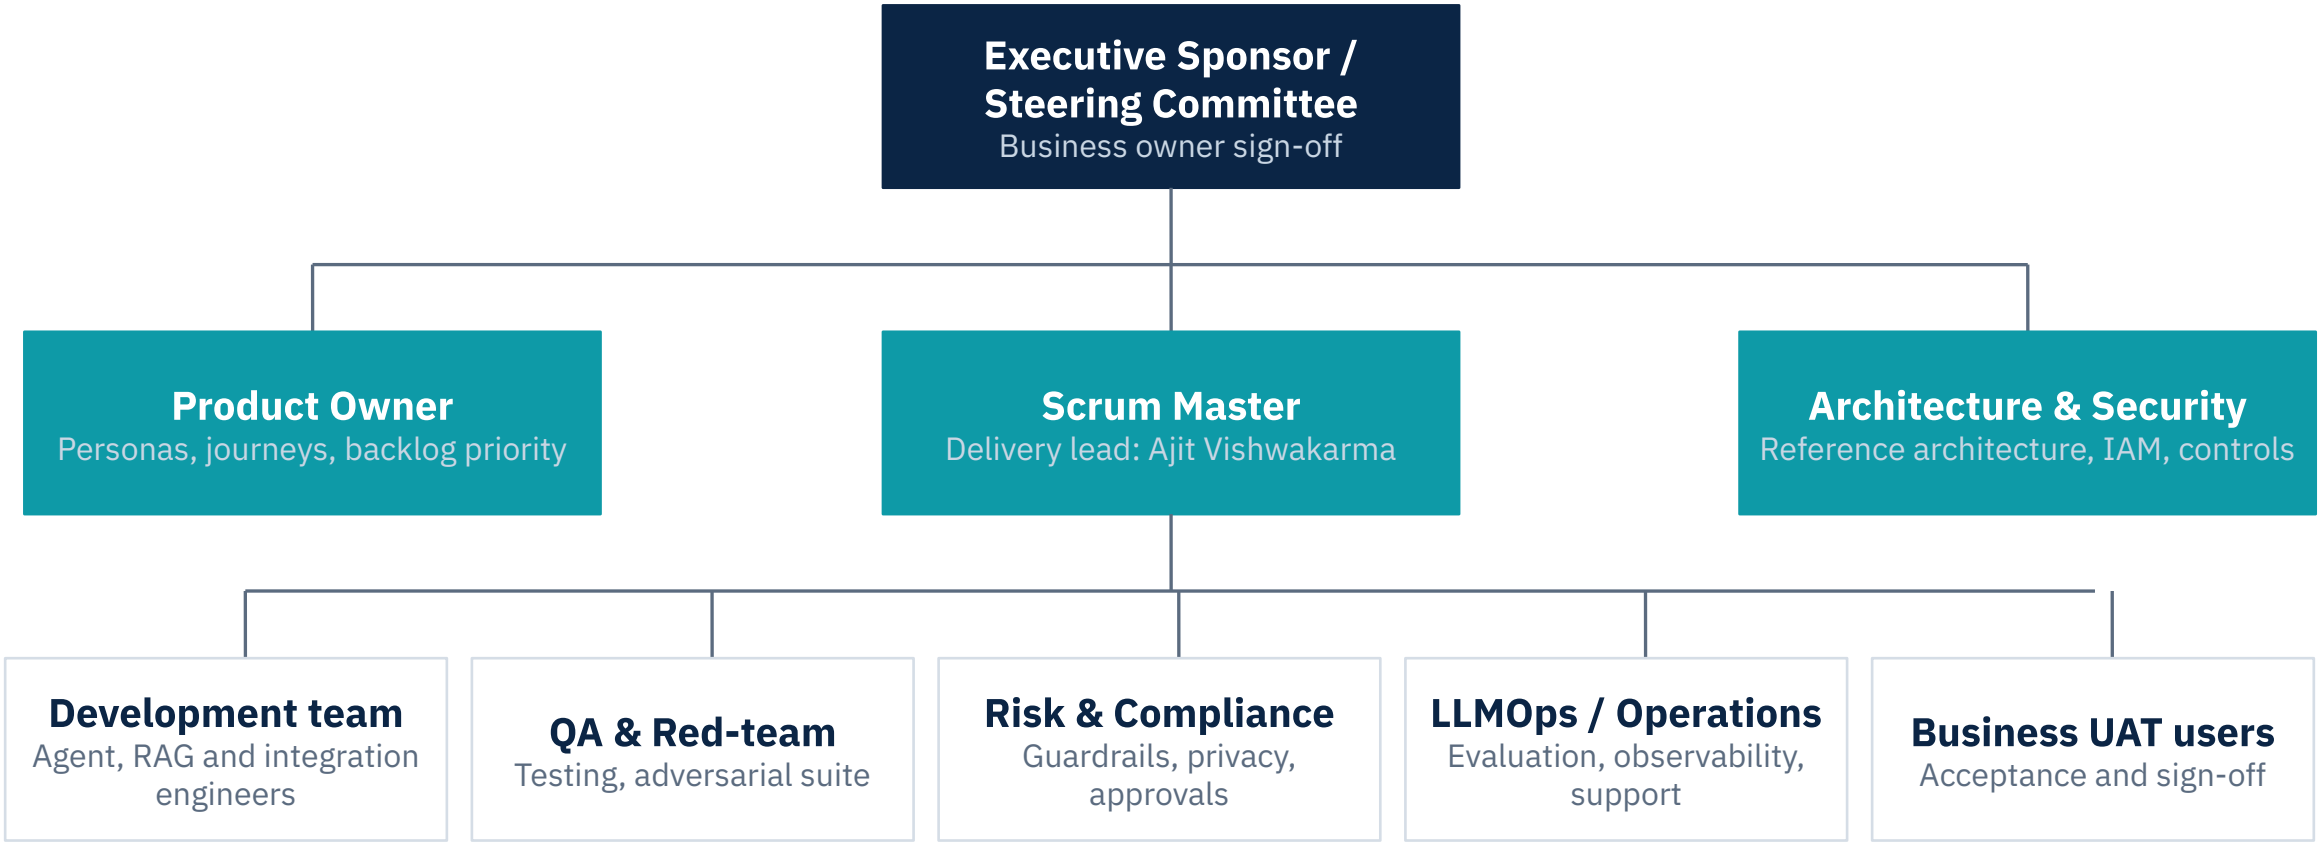

Escalation path: Team → Scrum Master → Product Owner → Steering Committee

Recommended reporting cadence

Forum	Cadence	Audience	Output	Jira report
Daily stand-up	Daily	Scrum team	Blockers and impediments	**Sprint board**
Sprint planning	Start of each 2-week sprint	Team + Product Owner	Sprint goal, committed backlog	**Backlog**
Sprint review & demo	End of each sprint	PO + stakeholders	Increment demo	**Sprint report**
Retrospective	End of each sprint	Scrum team	Improvement actions	**Velocity**
Release / steering status	Per release: v0.1, v0.5, v1.0	Steering Committee	Release status and risks	**Burndown, dashboard**

Recommended operating rhythm. Burndown, sprint report, velocity and the management dashboard are listed as “Recommended” Jira features in workbook 16_JIRA_FEATURES.

Risks to watch and the next steps in Jira

TOP RISKS

High	v1.0 deploy (BAS-39) has three blockers: BAS-26, UAT sign-off BAS-37 and privacy bug BAS-34. All are planned in S3–S5.
Med	Prompt injection and privacy defects (BAS-29, BAS-34). Red-team suite BAS-36 must pass before release.
Med	Tight December window: S6 ends 28 Dec and v1.0 releases the next day, 29 Dec.

NEXT STEPS

1. Assign owners: work items are unassigned
2. Tag fixVersions v0.1 / v0.5 / v1.0
3. Configure the review-gate workflow
4. Remove “BAS Sprint 1”; start S1
